

URBAN GLOW GRID

Weekly Team Meeting · Week 9 · Innovation Project



JUNE
12

Friday, June 12th, 2026

Weekly check-in #9 — Urban Glow Grid team

18:00

→ 19:15

75 min

AGENDA

TIME	TOPIC	OWNER
18:00	Opening & Review of Meeting #8 Action Items	All
18:15	Hardware Wiring Status & MOSFET Calibration Troubleshooting	Sofiane / Abir
18:40	Paris Model Architectural Final Adjustments	Mohamed
19:00	Integration & Presentation Prep Planning	All

ATTENDEES



Abir ISLAM
CEO / Project Lead




Sofiane LACHHAB
CTO / Physical Planner



Mohamed MELLOUK
Creative Director

PROJECT PROGRESS — WEEK 9

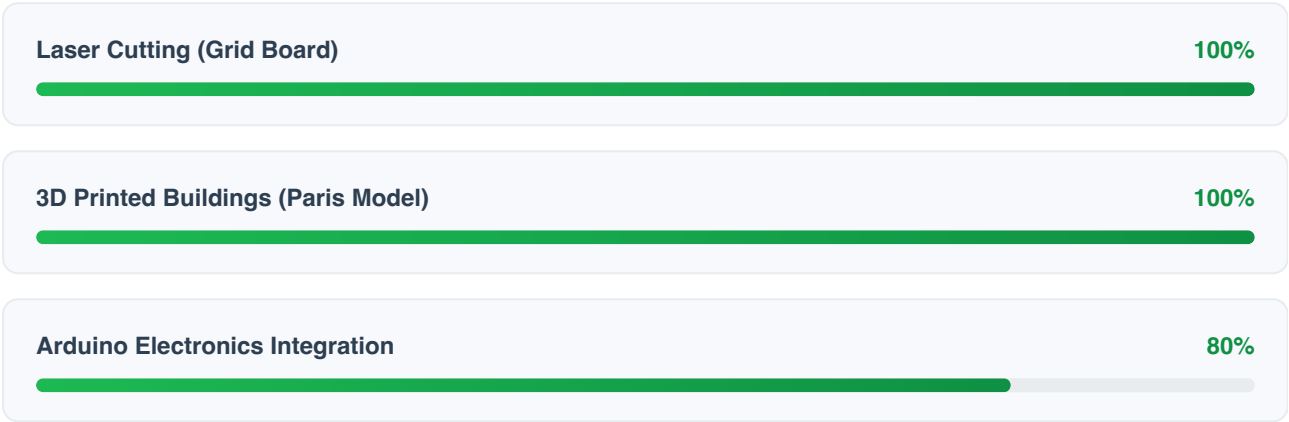

KEY DISCUSSIONS

MAIN FOCUS

Wiring & Code Calibration

STATUS

Minor Hardware Debugging

NEXT TARGET

System Integration Dry Run

Project Advancement — Meeting #9

- **Minor Wiring Issues:** Sofiane completed wiring for 5 out of the 6 dimmable zones. However, during testing of the 6th zone (residential sector), we encountered a short circuit due to stripped insulation in the wooden guide channel. Fixing this required minor disassembly.
- **Arduino Sketch Flashed:** Abir flashed the initial control sketch successfully. A minor issue was noted where input from the potentiometers (representing simulation speed and consumer load) fluctuates slightly on the analog inputs.
- **Analog Input Noise Resolution:** The team discussed adding a simple moving average software filter to the Arduino sketch to smooth out potentiometer readings and prevent flickering of the LED sectors.
- **Presentation Slides Iteration:** Mohamed continued slide editing, integrating simulator visual elements, but physical integration remains blocked until the 6th zone's wiring is repaired.

ACTION ITEMS TRACKER

#	TASK	OWNER	DUE	STATUS
1	Troubleshoot and fix 6th zone short circuit	Sofiane	June 15	Open
2	Implement software moving average filter in Arduino sketch	Abir	June 15	Open
3	Finalize slide layouts and defense speech draft	Mohamed	June 16	Open
4	Complete final wiring of all 6 dimmable zones (from Mtg #8)	Sofiane	June 8	In Progress
5	Flash Arduino with the finalized control sketch (from Mtg #8)	Abir	June 8	Done ✓
6	Dry run integrated presentation and physical tests (from Mtg #8)	All	June 9	Open

